R&N Platform Change Overview 03/12/18

2018 | 2019 | 2020

Sept | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | March | April | May | June | July | August

Future Release

100%

Release 2 XRN4361

- PIS

100%

Release 3 XRN4572

- T1 – UAT
- T1 – MT
- T1 – PT
- Imp
- T1 – RT
- T2 – testing
- Imp
- Closedown
- T2 – MT
- T2 - ST
- T2 – UAT

Feb 19

- Implementation

0%

June 19

- Governance
- Detailed Design
- Build
- System Test
- SIT
- UAT
- Imp Prep
- Go Live
- PIS

0%

EUC – XRN4665

- Mobilisation
- Detailed Design
- Build
- System Test
- UAT
- PT
- RT
- Imp #1
- PIS
- Imp #2
- PIS

Mod 621

- MOD 621 UKLP CUT
- MOD 621 UKLP ST
- MOD 621 UKLP AT & RT
- MOD 621 UKLP Code Merge
- UMOD 621 KLP PT
- MOD 621 UKLP Go Live

0%

November 19

- Capture
- Start Up
- Detailed Design
- Build & Unit Test
- ST
- SIT
- UAT
- Market Trials
- Cutover, Imp (inc. IDR)
- PIS

100%

Minor Release

- PIS
- MR Drop 3 Design
- MR Drop 3 Build
- MR Drop 3 Test
- IMP
- PIS
- Design (B), Build(B) & Test (A) Drop 2
- IMP
- PIS

CSSC XRN4584

- Level 2 IA
- Procurement
- Delivery

UK Link Programme

Data Archival XRN1154

- IMP
- PIS
- OTF

R&N Platform Change Overview 21/11/18

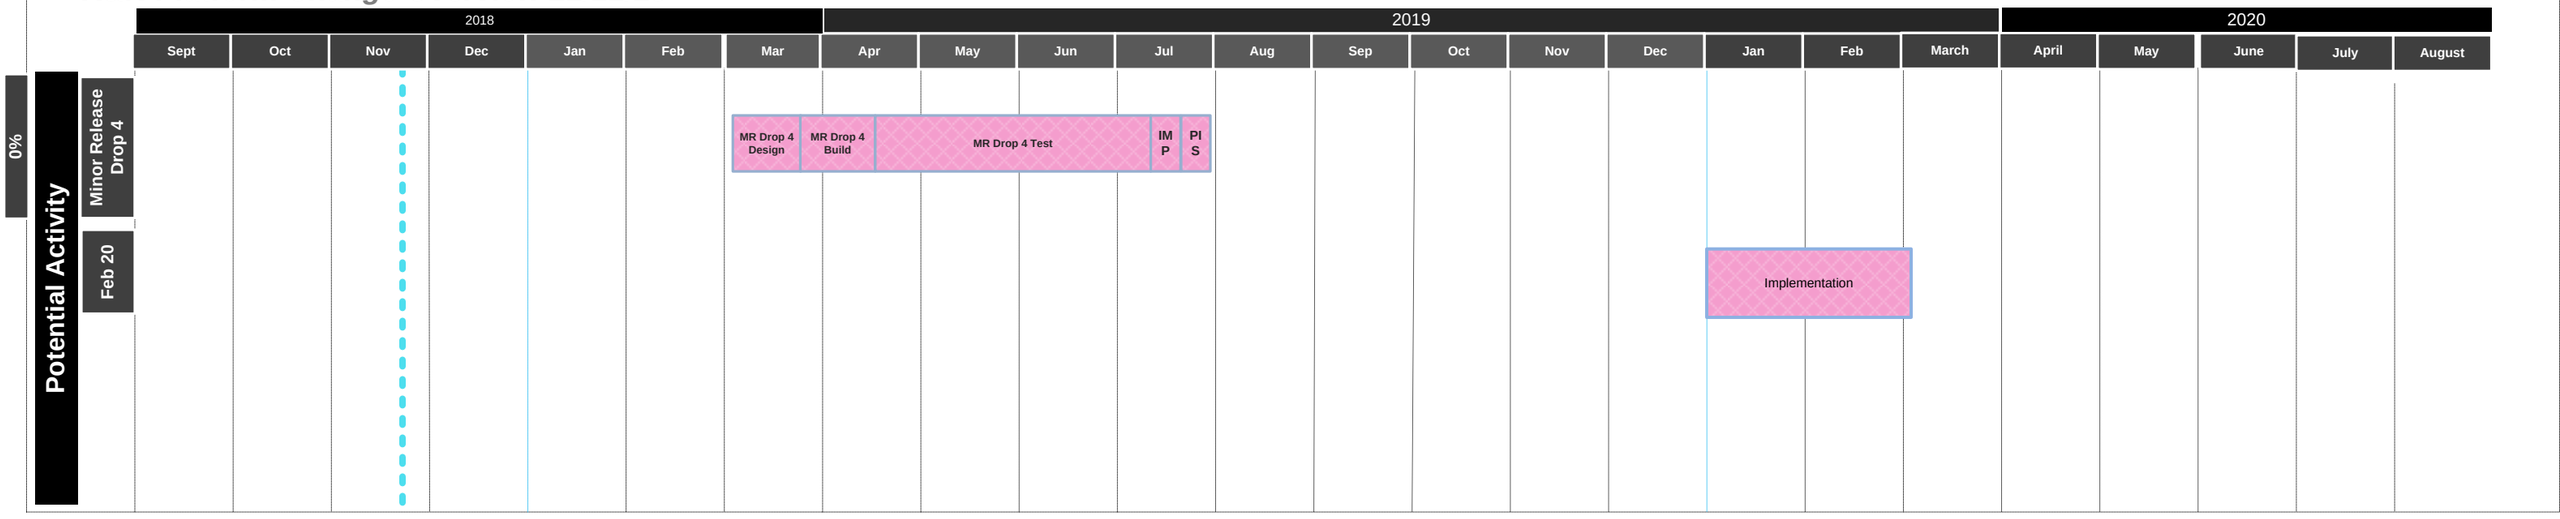

Key:

- XXX — Completed Activity
- XXX — Forecast Activity
- XXX — Original Baselined Activity
- XXX — Potential Activity
